

DEVELOPMENT PROGRESS REPORT

ParSU e-Feedback System

Complaint & Feedback Management Platform for Partido State University

50% COMPLETE

Prepared for: **Project Stakeholders & Review Panel**

Reporting period: **Development Phase — Mid-Cycle Checkpoint**

Date: **August 18, 2026**

Agenda

01

Project Overview

Purpose, scope, and target users of the platform

02

Progress at a Glance

Overall completion status and delivery snapshot

03

Completed Modules

Features that are built, tested, and functioning

04

Work In Progress & Remaining

What is left before full delivery

05

Technical Foundation

Architecture, stack, and data model

06

Timeline & Next Steps

Path to completion and upcoming milestones

Project Overview

ParSU e-Feedback is a web-based complaint and feedback management system that lets students file, track, and rate the resolution of concerns, while staff, deans, quality assurance officers, and administrators manage routing, response, and reporting across offices.

Student	Submit complaints, attach evidence, track status, rate resolutions
Staff	Receive assigned tickets, update status, communicate with students
Dean	Oversee office performance, reassign tickets, view analytics
Quality Assurance	Monitor SLA compliance, review feedback, generate reports
Admin	Manage users, offices, categories, routing & SLA rules

PROJECT SNAPSHOT

PLATFORM

Next.js web application

USER ROLES

5 (Student, Staff, Dean, QA, Admin)

CORE WORKFLOW

Submit → Route → Resolve → Rate


REPORTING CYCLE

Phase 6 — mid-development


CURRENT STATUS

50% of planned scope complete

Progress at a Glance

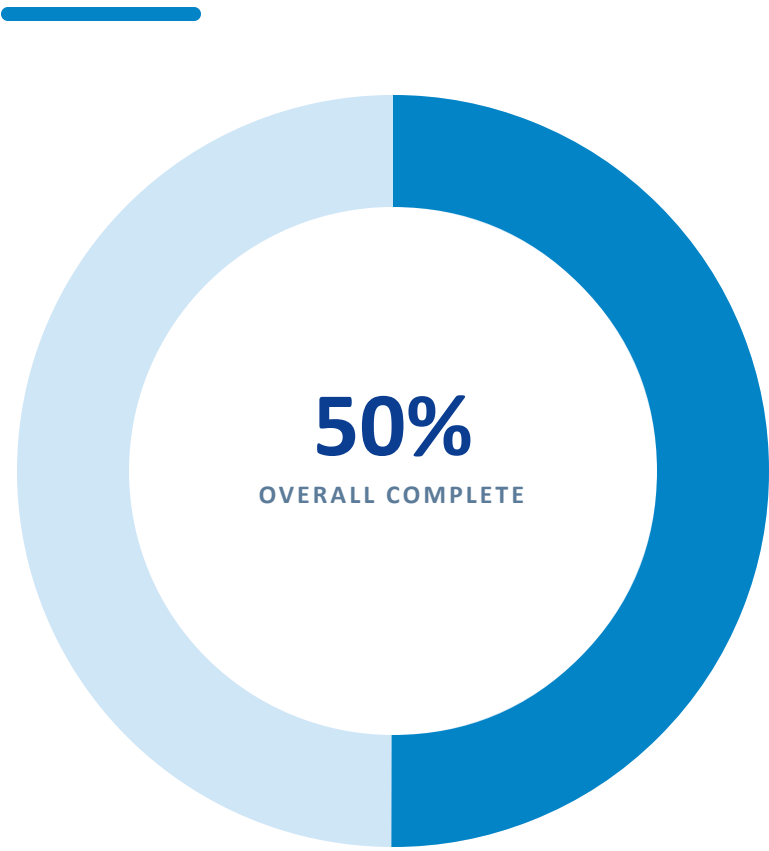

COMPLETION BY MODULE

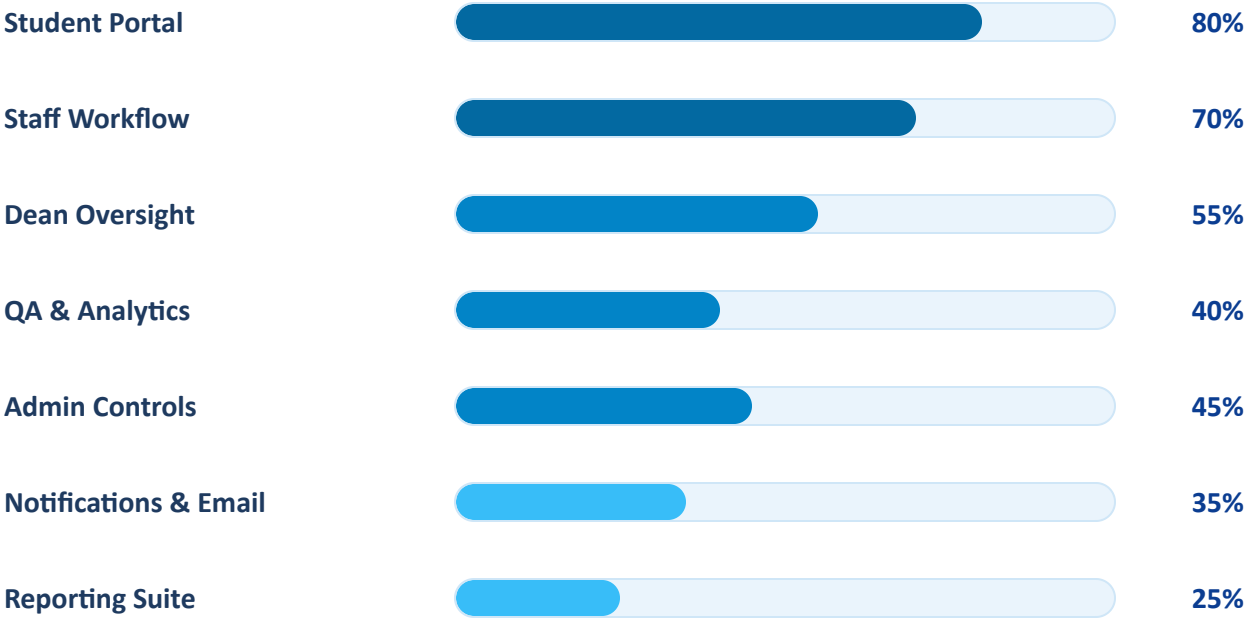

What's Done — Core Platform

COMPLETED

Authentication & Access

Registration, login, password reset, and role-based routing for all five user types are working end to end.

Complaint Submission

Students can file complaints with category selection, descriptions, and file attachments through a guided form.

Complaint Tracking

Students and staff can view complaint lists, filter/sort, and open a detailed timeline of each ticket.

Staff Resolution Workflow

Staff can self-assign tickets, update statuses, add internal notes, and message students.

Role-Based Dashboards

Each role (Student, Staff, Dean, QA, Admin) has a working dashboard summarizing relevant activity.

Database & Data Model

Core schema for complaints, users, offices, categories, attachments, and audit logs is finalized (see ERD).

What's Left — Remaining Work

IN PROGRESS

Analytics & Trend Reporting

40%

Charts for complaint trends and category/priority breakdowns are partially built; drilldowns still pending.

SLA Automation

45%

SLA rule configuration exists in the data model; automated breach detection and alerts are not yet wired up.

QA Feedback Review

30%

QA feedback listing page is scaffolded; scoring workflow and resolution-quality review are not implemented.

Admin Configuration Suite

50%

Offices, categories, and routing-rule screens exist but validation, bulk actions, and audit views need work.

Notifications & Email

40%

In-app notification panel is live; transactional email delivery and digesting are still being integrated.

Testing, Docs & Deployment

25%

Integration tests cover core flows only; production hardening and a deployment runbook remain.

Technical Foundation


TECH STACK

- **Frontend:** Next.js (App Router), React, Tailwind CSS
- **Backend:** Next.js API routes, server-side services layer
- **Database:** MongoDB with Mongoose data models
- **Auth:** Session-based auth with role-based access control
- **Infra:** Vercel deployment, scheduled cron for SLA checks

STATUS OF EACH LAYER

Data model	Stable
API routes	Core done, edge cases WIP
UI components	In progress

CORE DATA ENTITIES

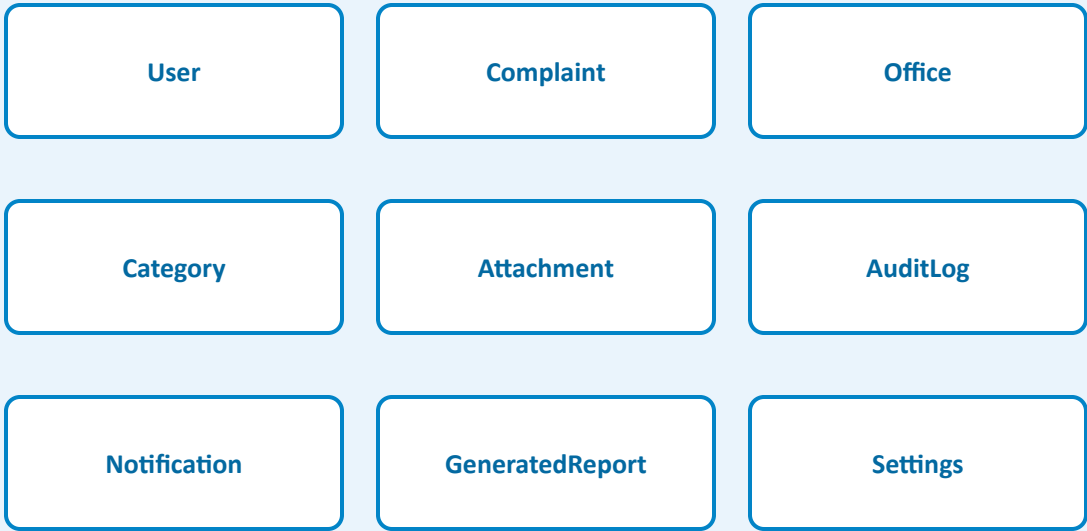

Full entity-relationship diagram available in project documentation.

Timeline & Next Steps



IMMEDIATE NEXT STEPS

- 1. Finish SLA breach automation & alerts
- 2. Complete QA feedback scoring workflow
- 3. Wire up email notification delivery
- 4. Expand analytics drilldowns
- 5. Increase automated test coverage

We're Halfway There

The core platform — authentication, complaint submission, and staff resolution — is live and working. The next phase focuses on analytics, automation, and reporting to bring ParSU e-Feedback to full completion.

Thank you

Questions & discussion welcome
